

MEMORANDUM

DATE: May 14, 2021


TO: Ellis Mitchell

FROM: Eric Kamps, EIT


RE: City of Benton Harbor Construction Project Updates

Northeast Section Reconstruction Project

Selge Construction continued on Phase 2 of the Northeast Section project this week. Sanitary sewer work included sewer main and sewer manholes west from Winans Street and along Nowlen Street this week. This completes the installation of the sanitary sewer main. Sanitary laterals are being continue to be placed. The installation of new water services also continue during the past week. Storm sewer installation also began this week.

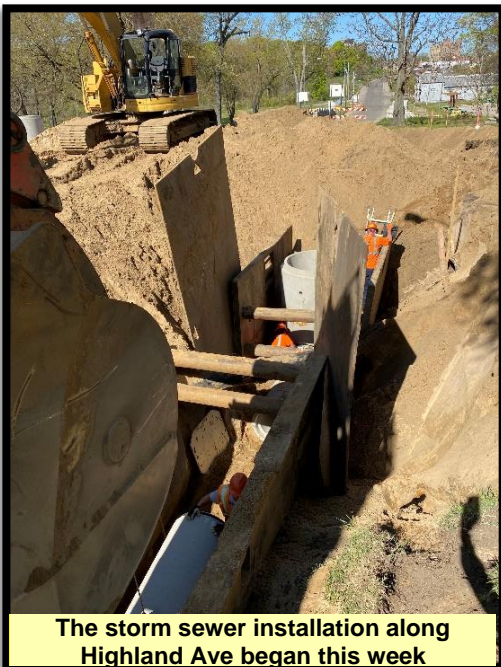

The storm sewer installation along Highland Ave began this week

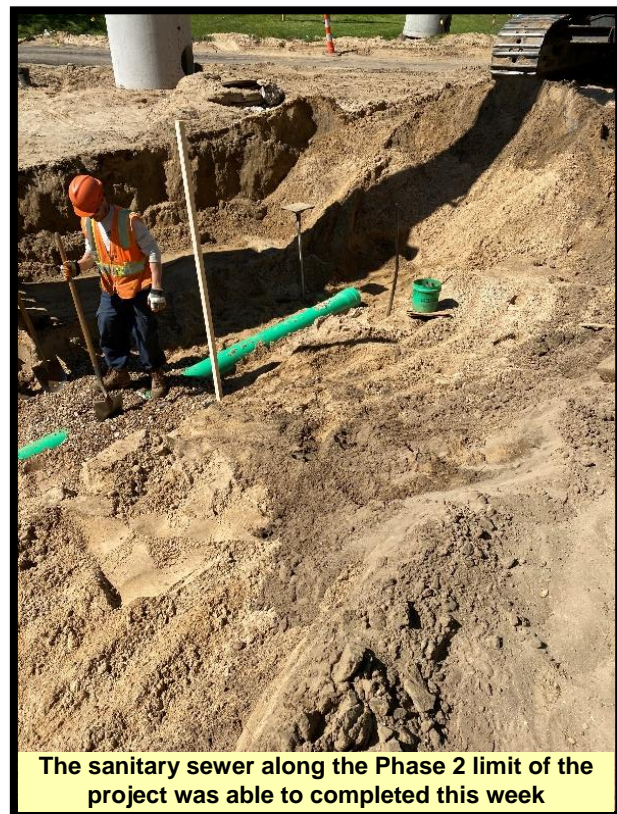


The sanitary sewer along the Phase 2 limit of the project was able to completed this week

Next week, the contractor will continue to work on the storm sewer along Highland Ave, working east from Hull Ave. They will also continue to complete all water service work and sanitary sewer lateral work needed. The contractor is also planning to start to grade Nowlen Street from Cass Street to Highland Ave. The project is scheduled to be completed by the Fourth of July.

Pipestone Street Corridor Reconstruction Project

Construction on the Pipestone Corridor Project Phase 2 and 3 continued this week. Kalin worked on the placement of the sanitary sewer along Wall Street between Pipestone Street and 4th Street. While placing the sanitary sewer main, the contractor also worked on placing new sanitary service laterals to each property. Duran Concrete installed concrete sidewalk ramps within the Phase 2 project limits to complete all concrete work in Phase 2. Kalin also worked this week to complete the restoration of the disturbed areas in the Phase 1 and 2 limits.


Next week, Kalin plans to continue the installation of sanitary sewer within the Phase 3 limits on Wall Street. Once complete, they will begin work on the installation of the water main in the Phase 3 limits. Restoration of the Phase 1 and 2 limits along Pipestone Street will also continue in the upcoming weeks.

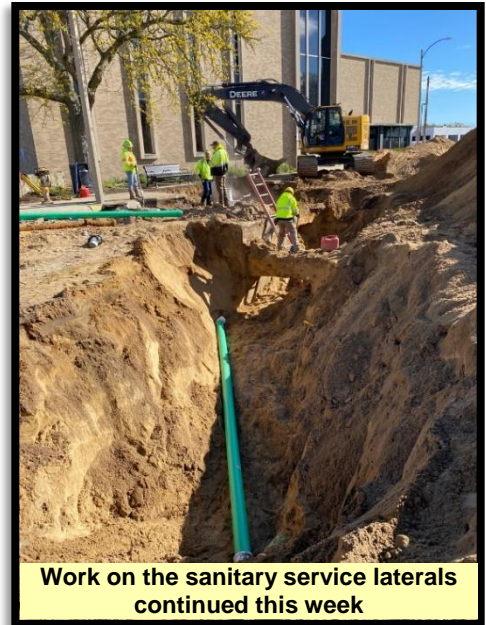

Maple Street and Vineyard Avenue Reconstruction Project

Northern Construction Services began the sanitary sewer installation along Vineyard Ave. While installing the sewer main, the contractor also worked to place sanitary sewer laterals to all the property that they cross. As the Contractor completes installing the new sanitary sewer, the trench is backfilled and compacted. Northern Construction also worked on completing water services to all the properties.

Next week, sanitary sewer along Vineyard Ave will continue, along with the sanitary sewer laterals. The contractor is also hopeful to start the storm sewer along Maple Street. This project will continue throughout the summer.

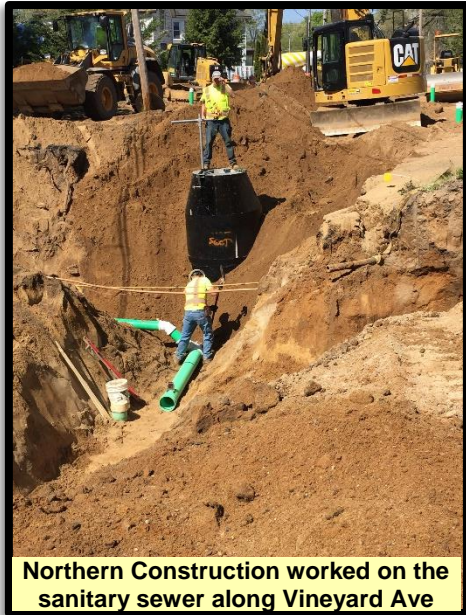

As work along projects begin, information will be added to the weekly project update. If you have any project questions or would like to be added to the email list for project updates, please contact Eric Kamps of the project team at ekamps@abonmarche.com or (269) 926-4556.

